



OrderFlow Nexus

(Order & Vendor
Coordination System)

Debal Adhikari
April 8th

Situation

(The "As-Is" State)

Current Workflow: The procurement and order processing lifecycle currently manages a high volume of 2,321 orders.

Coordination Landscape: Manual alignment between client timelines and procurement vendors across various print techniques.

Performance Monitoring: Ad-hoc support and manual feedback collection for Customer Satisfaction (CSAT).



Problem

(The Gap)

Communication Silos: Lack of a centralized module to align timelines between clients and vendors, leading to potential fulfillment delays.

Inefficient Assignment: No standardized analysis of vendor capabilities or print techniques, resulting in sub-optimal vendor selection.

Recurring Issues: Order-related problems are often addressed reactively without a structured Root Cause Analysis (RCA) framework to prevent recurrence.

Visibility Gaps: Inconsistent monitoring of KRAs and KPIs like delivery accuracy and issue resolution time.



Opportunity

(The "To-Be" State)

Unified Nexus: A centralized "OrderFlow Nexus" that automates the order lifecycle from placement to final delivery.

Intelligent Optimization: Data-driven vendor assignment based on specific technical capabilities and capacity.


Proactive Resolution: A dedicated escalation module that utilizes RCA to institutionalize process improvements.

Real-time Insights: A live Performance Dashboard providing instant visibility into delivery accuracy and vendor performance.



Purpose Statement

To implement an Agile-based OrderFlow Nexus system that streamlines the coordination between 2,300+ orders, clients, and vendors, ensuring 100% timeline alignment and improved service quality through data-driven optimization.

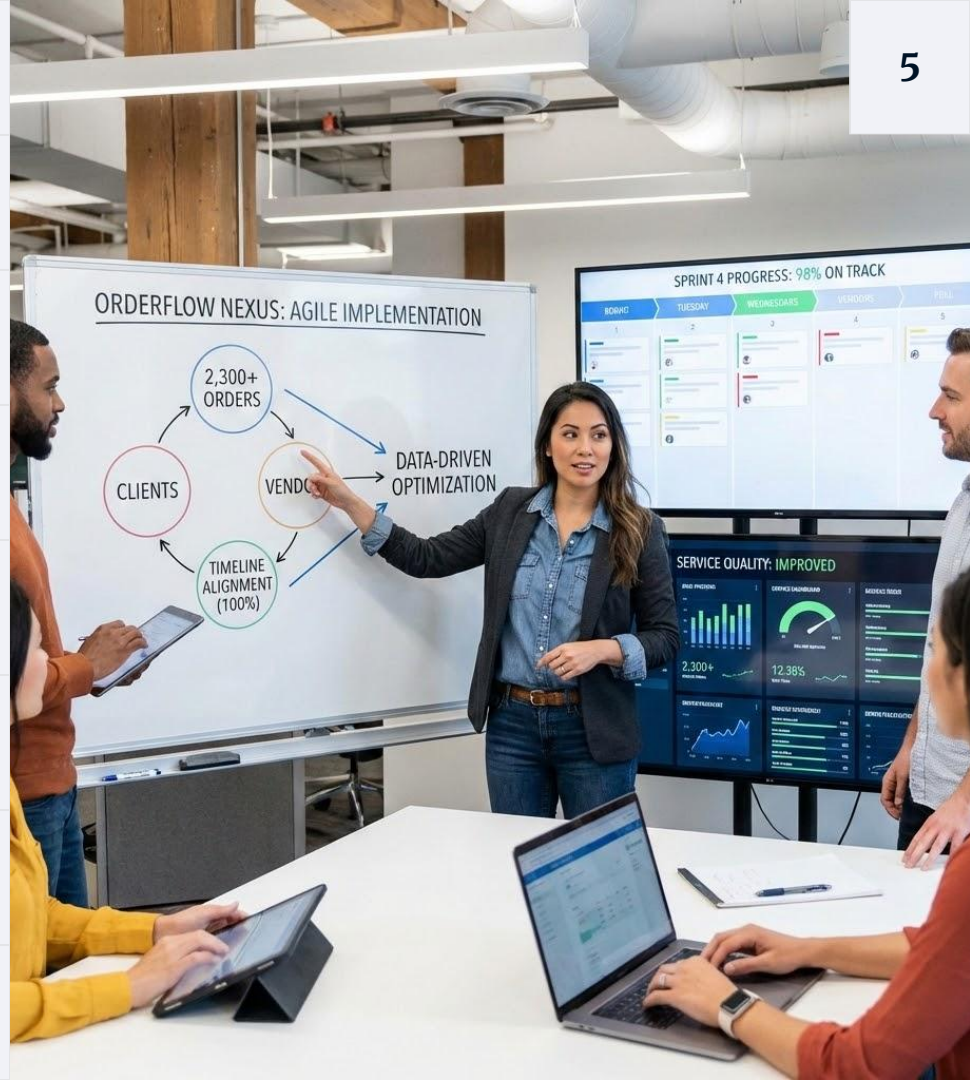

Project Objectives

Feature 1: Deployment

Establish a Vendor & Client Coordination Module to synchronize procurement timelines.



Feature 2: Optimization Engine

Build an assignment logic that matches orders to vendors based on print techniques and capabilities.



Project Objectives



Feature 3: Resolution Framework

Implement an automated Issue Resolution and Escalation system using RCA.



Feature 4: Metrics Integration

Develop a Performance Dashboard to track KRAs including CSAT and Delivery Accuracy.



Success Criteria

8



Specific

Achieve a 15% reduction in order-related errors by the end of the second quarter post-launch by utilizing automated vendor capability matching.

Achievable

Maintain a minimum Customer Satisfaction (CSAT) score of 4.2/5.0, measured via the integrated feedback tracking module.


Realistic

Ensure 100% of the active 2,321 orders are managed exclusively through the Nexus platform within 30 days of the "Go-Live" date.

Time-bound

Reduce the average "Issue Resolution Time" by 25% within the first 6 months of implementation through the systematic use of the vendor assignment framework.

Success Criteria

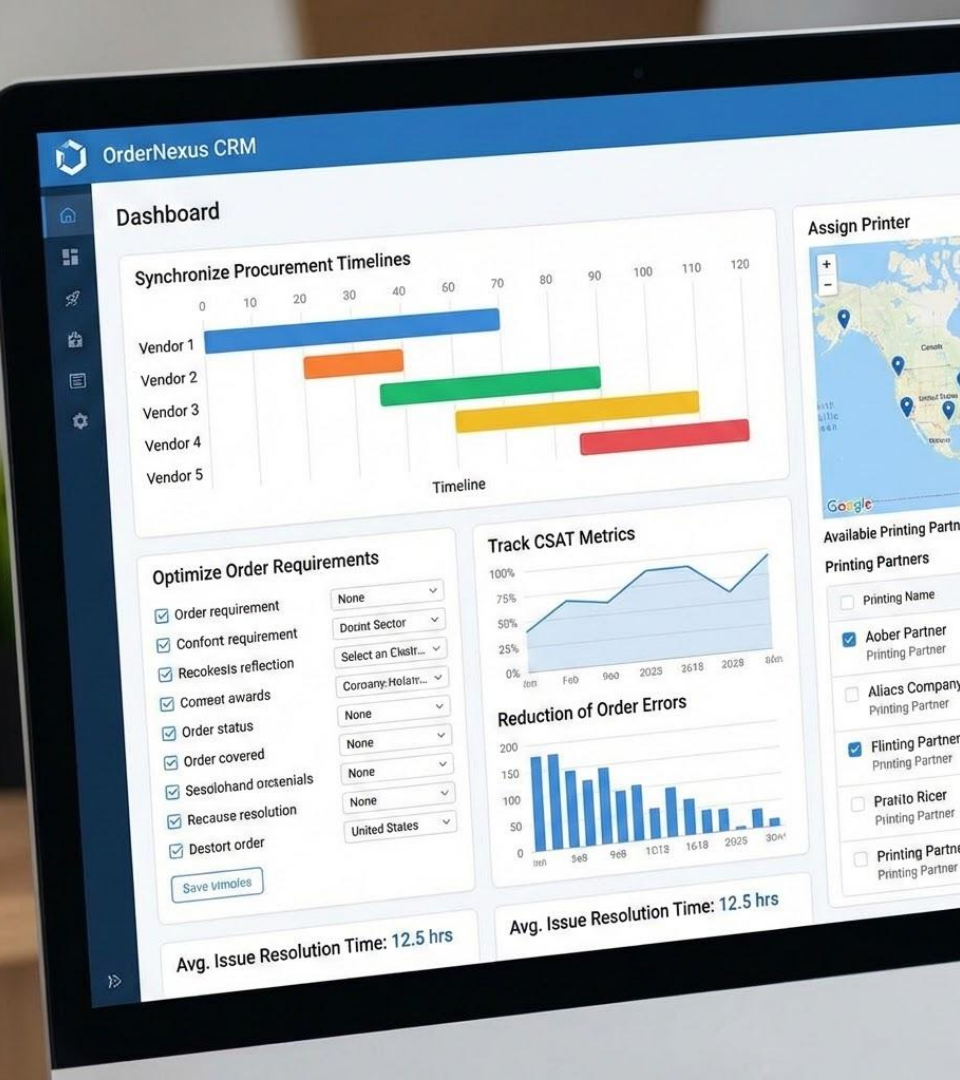

Vendor & Client Coordination Module

100% synchronization of procurement timelines. Zero "timeline conflict" alerts per sprint after the feature stabilizes.

Vendor Assignment Optimization

Accuracy of technical matching. A 20% increase in orders assigned to "Best Fit" vendors based on print technique analysis rather than manual selection.

Issue Resolution & Escalation Handling

Recurrence rate of critical issues. Identification of at least 5 major recurring process bottlenecks through RCA, leading to a measurable drop in escalated tickets.

Performance Dashboard

Data visibility and reporting. 100% availability of real-time delivery accuracy and vendor performance metrics for stakeholders during every Sprint Review.

Project Approach

Iterative Development: The project is divided into 2–4 week Sprints, ensuring that functional components of the coordination system are delivered and demonstrated early and often.

Requirement Management: Utilizing a Product Backlog to prioritize the four core features, allowing for flexibility as vendor requirements or print technique complexities evolve.

- Daily Stand-ups
- Sprint Reviews
- Sprint Retrospectives
- Backlog Refinement



Project Approach

11



Sprint 1-2 (Foundation)

Setup of the Order Lifecycle Management engine to track the 2,321 orders from placement to delivery.

Sprint 3-4 (Coordination & Assignment)

Development of the Vendor & Client Coordination Module and the Vendor Assignment Optimization logic based on print technique analysis.

Sprint 5-6 (Resolution & Quality)

Integration of the Issue Resolution & Escalation Handling module, incorporating the Root Cause Analysis (RCA) toolkit.

Sprint 7-8 (Monitoring & Analytics)

Launch of the Performance Dashboard (KRA & KPI) and the Customer Satisfaction (CSAT) Tracking module.

Project Approach

1. Requirement Gathering & Backlog Grooming:

Translating functionalities into granular User Stories and prioritizing them by business value in the Product Backlog.

2. Sprint Planning:

Selecting a subset of high-priority stories and breaking them into specific technical tasks for a 2-week work cycle.

3. Execution (Development & Daily Stand-ups)

Conducting 15-minute daily syncs to track coding progress and remove immediate blockers for the development team.

5. Sprint Retrospective:

Analyzing internal team processes to identify what went well and implementing improvements for the following sprint cycle.

4. Sprint Review (Demonstration):

Showcasing working features, such as the Performance Dashboard, to stakeholders to gather immediate feedback and validation.

6. Deployment & UAT (User Acceptance Testing)

Validating the integrated system with end-users to ensure the assignment logic and RCA tools meet operational needs before go-live.

Resource Estimation

13

People
(7–8 members)

Project team members from client community and ITS, including a Scrum Master, Product Owner, and Development Team.

Time
(4 months)

Implementation within 4 months (8 two-week Agile Sprints).

Budget
(Rs 5 Lac)

Hardware, software, training, and services not to exceed Rs. 5 Lac.

Other

Third-party software evaluation, vendor site visits, and performance tracking tools – not to exceed Rs. 1.5 Lac.

Risks and Dependencies

Data Integrity

Success depends on the accuracy of vendor capability data provided for the optimization engine.

Stakeholder Adoption

Effectiveness of the Coordination Module relies on vendors and clients actively using the system for timeline updates.

Technical Complexity

Integration of real-time tracking for 2,300+ concurrent orders requires high system uptime and performance.

Legacy Process Resistance

The current coordination and vendor assignment methods have been in place for a significant period; transitioning to an automated Agile system may face resistance from users accustomed to manual workarounds.



Thank You!

